First Capitol Dr. Enhancements | Update 12-31-17_1 | 19-Jan-18 13:38

Activity ID	Activity Name	Early Start	Early Finish
A1000	Layout for waterline	20-Dec-17	21-Dec-17
A1010	Sawcut for Waterline 5th - 3rd	22-Dec-17	22-Dec-17
A1020	Expose main at 4th for EZ Valve connections	26-Dec-17	27-Dec-17
A1100	Install EZ Valves at 4th Street	22-Jan-18	23-Jan-18
A1030	Waterline construction 5th to 3rd	24-Jan-18	06-Mar-18
A1050	Sawcut Waterline 3rd to Main	07-Mar-18	08-Mar-18
A1040	Water Services 5th to 3rd	07-Mar-18	20-Mar-18
A1060	Waterline 3rd to Main	09-Mar-18	19-Apr-18
A1080	Storm Sewer and Drainage Structures	21-Mar-18	17-Apr-18
A1090	Set up southern traffic shift	18-Apr-18	19-Apr-18
A1070	Water services 3rd to main	20-Apr-18	03-May-18
A1120	southern irrigation work	20-Apr-18	10-May-18
A1130	southern underground electrical work	20-Apr-18	12-Jul-18
A1110	Southern sidewalk, bio areas and other items	20-Apr-18	16-Jul-18
A1160	irrigation north side	11-May-18	31-May-18
A1170	underground electric north side	01-Jun-18	23-Aug-18
A1150	southern pavers	17-Jul-18	23-Jul-18
A1140	Remove south shift and set up north shift	24-Jul-18	26-Jul-18
A1180	sidewalk, bio areas, north side	26-Jul-18	22-Oct-18
A1200	lights installed	24-Aug-18	06-Sep-18
A1190	pavers north side	22-Oct-18	29-Oct-18
A1210	mill pavement	29-Oct-18	31-Oct-18
A1220	surface asphalt	31-Oct-18	02-Nov-18
A1230	landscaping, sod, etc.	02-Nov-18	16-Nov-18
A1240	signing and fencing	02-Nov-18	16-Nov-18
A1250	striping to final configuration	16-Nov-18	23-Nov-18
A1260	final cleanup	23-Nov-18	30-Nov-18
A1270	demobilize	30-Nov-18	03-Dec-18

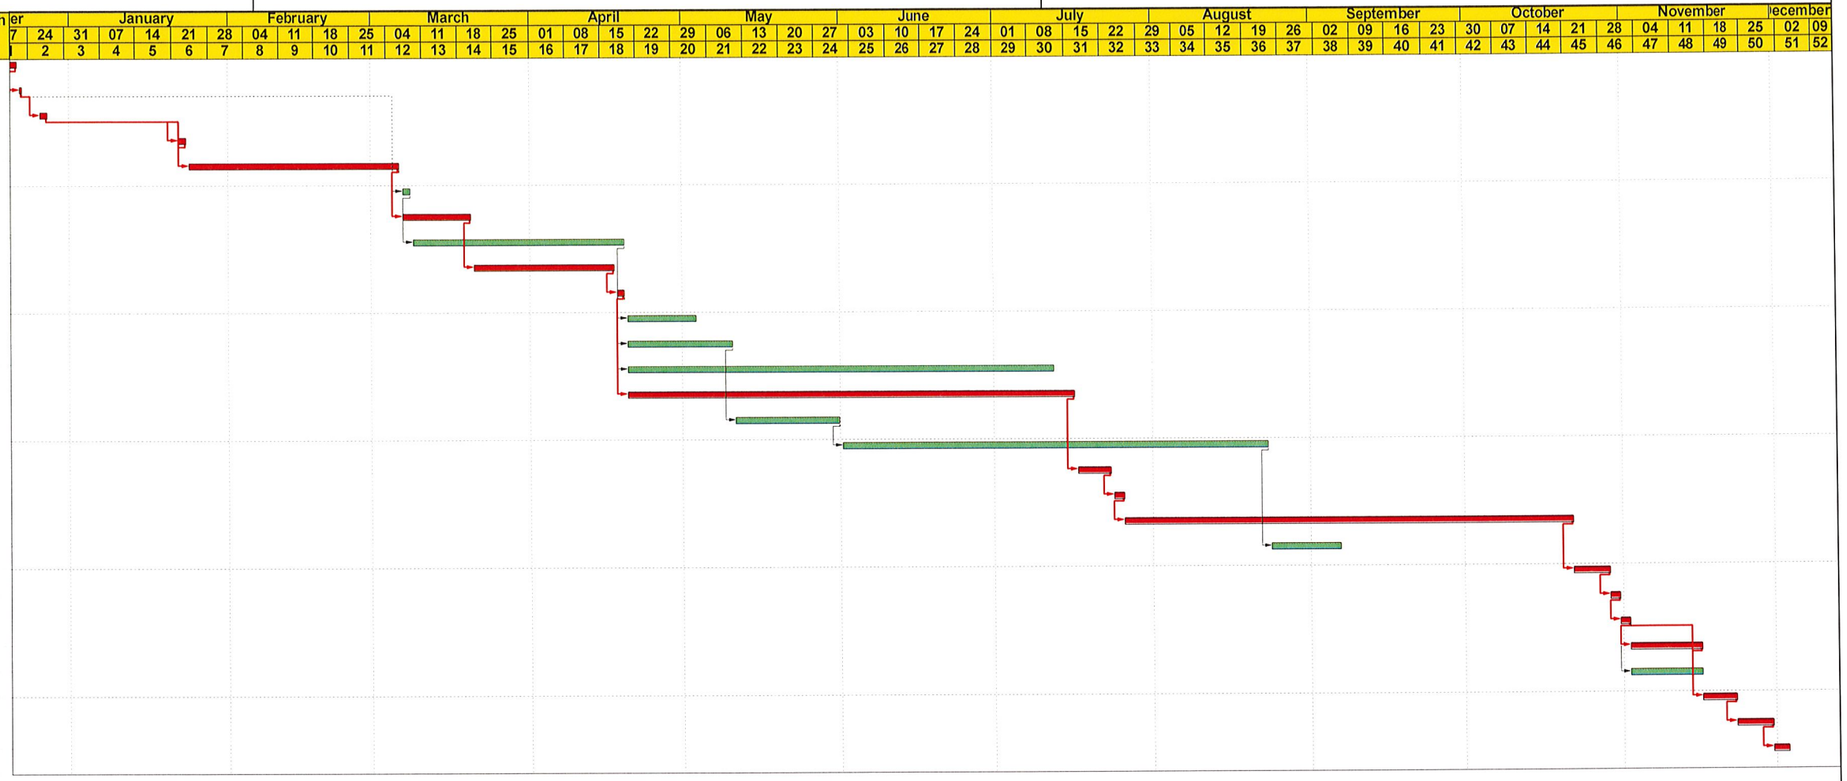

Actual Work
Remaining Work
Critical Remaining Work
Milestone

First Capitol Enhancements

CITY OF ST. CHARLES

Updated Schedule 1/19/18

GERSHENSON CONSTRUCTION COMPANY, INC.

2 TRUITT DR

EUREKA, MO 63025
